# MEASURE P BOND PROGRAM INFORMATION

Report Date PE: June 30, 2021

## **Measure P Phase 1 Summary**

#### Phase 1 Project Sequencing:

- Rancho Campus
  - New Library/Learning Commons
  - MACC Renovation
  - Swimming Pool Renovation
  - Campus-wide Boiler Replacement
  - Old Library TI (for swing space use during Measure P implementation)
  - New Campus Center
     Students Services Building
- Chino Campus
  - Instructional Building 1
  - Chino MIB Secondary Effects
- Fontana Campus
  - Campus Parking and Vehicular Circulation
  - Welcome Center/Library
  - Instructional Building 1
  - Automotive Tech Building
  - Operations and Maintenance Building
- Ontario Campus
  - Master Planning
  - Campus Development

# MEASURE P IMPLEMENTATION ACTIVITIES SUMMARY

#### Measure P Funding Update Summary:

- First Bond Issuance Resolution
  - \$200 million; Receipt of bond proceeds on September 24, 2019
- Refunding Resolution (Measure L)
  - Refunded \$50 million+, saving taxpayers over \$6 million on their Measure L tax bills.

#### Consultant Procurements (Program Level):

- Commissioning Consulting Services- Completed
- Stormwater Pollution Prevention Planning (SWPPP) & Civil Engineering Consulting Services- Completed

## Phase 1 Project work Update:

- Rancho campus:
  - New Library/Learning Commons Project- Design Build Criteria package completed; Two step Design Build Entity procurement in work: Step 1- Design Build Request for Qualifications (RFQ); Step 2- Request for Proposals (RFP) to follow
  - MACC Renovation- Programming with Core team and Work group ongoing; Preliminary Estimates in work; Schematic Design to follow
  - Swimming Pool Renovation- Programming with Core team and Work group ongoing; Preliminary Estimates in work;
     Schematic Design to follow
  - Campus-wide Boiler Replacement project- AE & consultant firms working on DSA submittal for the project

#### • Chino campus:

- Constructability Review comments reviewed and being addressed with DSA back check response
- DSA back check comments response completed, DSA approval awaited; Ca Community College Chancellors Office State funding 'Bid and Award' approvals to follow


#### • Fontana NEW campus:

- Parcel (lot) consolidation process ongoing
- New Campus Master Plan approved at June 24, 2021 Governing Board Meeting
- Ontario NEW campus:
  - Land Acquisition completed

## **Program Funds/Measure P Bond Funds**

#### **Program Funds**


(Includes Rancho Cucamonga, Fontana and Chino Campuses)

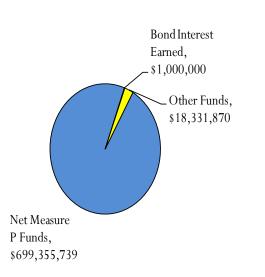

Fund Source	Amount	Percentage of Total
Original Measure P Bond	\$700,000,000	97.40%
Less Cost of Issuance	(\$644,261)	-0.09%
Net Measure P Funds	\$699,355,739	97.31%
Bond Interest Earned	\$1,000,000	0.14%
Other Funds	\$18,331,870	2.55%
Total Program Funds	\$718,687,609	100.00%

#### **Measure P Bond Funds**


(Includes Rancho Cucamonga, Fontana and Chino Campuses)



Fund Source	Amount	Percentage of Total
Original Measure P Bond	\$700,000,000	99.95%
Less Cost of Issuance	(\$644,261)	-0.09%
Net Measure P Funds	\$699,355,739	99.86%
Bond Interest Earned	\$1,000,000	0.14%
Total Measure P Bond Funds	\$700,355,739	100.00%

## **Program Funds**


(Includes Rancho Cucamonga, Fontana and Chino Campuses)



/ 0	Total Program Funds	\$718,687,609	100.00%
/ 0 / 0	Committed (Expensed or Encumbered)	\$45,383,420	6.31%
⁄o ⁄o	Allocated to Projects	\$672,304,189	93.55%
0	Remaining Balance	\$1,000,000	0.14%

#### **Measure P Bond Funds**

(Includes Rancho Cucamonga, Fontana and Chino Campuses)



Total Measure P Bond Funds	\$700,355,739	100.00%
Committed (Expensed or Encumbered)	\$41,217,326	5.89%
Allocated to Projects	\$658,138,413	93.97%
Remaining Balance	\$1,000,000	0.14%

## **PROJECTS IN PROGRESS**

RANCHO LLC Rendering (elevations subject to change)



CHINO IB Building View



#### FONTANA Master Plan (elevations subject to change)



# **UPCOMING ACTIVITIES**

- Facilities Master Plan Vision 2025 & Addendum- COVID impacts forced College Hybrid Learning Environment, associated revisions to campus Built Environment reviewed, changes, and implementation ongoing;
- Rancho and Chino campus- ADA Barrier removal project drawings, DSA submittal discussions ongoing;
- Rancho campus: CEQA-EIR process ongoing;
- Rancho campus Utility Capacity determination
- Fontana campus: CEQA-EIR proposal solicitation ongoing;
- Ontario campus- Topography and Design survey;
